



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

CONSTRUCTION UPDATE #19

Week of August 5, 2024

Hi Everyone!

Construction has begun and these updates will be distributed regularly to keep the community up to date on the status of the projects. Thanks in advance for everyone's understanding and patience during construction.

Current Period

- Contractor started forming and pouring the new curb, gutter, sidewalk, and driveways on the south side of Broadway.
- Contractor relocated the pedestrian push button at southeast corner of Blairs
- Night crew continued with the installation of the new 8-inch sewer line and manholes for the new sewer main that runs down the center of Broadway
- Traffic control measures will be in place to direct vehicles and pedestrians through the work areas, but there may be some minor delays.
- **Businesses near the project site and their access will remain open during all stages of construction.**

Following Period

- **NIGHT WORK** - To help alleviate traffic congestion near the Broadway and Mosquito Road intersection, the Contractor will continue work operations to install the new 18-inch sewer and manholes down the center of Broadway. ***This work will continue for approximately 5 more weeks.***
- **DAY WORK** – Contractor will continue work operations on the south side of Broadway from Blairs to the east with the forming and pouring of the new curb, gutter, sidewalk, and driveways. Once the south side surface improvements are done daytime work will be minimal.

Important Information

HWY 50 eastbound off-ramp at Broadway and Mosquito Road under HWY 50 will be closed at night due to nighttime work operations at the intersection of Mosquito Road and Broadway.

Contacts

Dion Carr, Resident Engineer, Dewberry, (916) 276-4721, dcarr@dewberry.com

Melissa McConnell, City Engineer, City of Placerville, (530) 642-5250, mmcconnell@cityofplacerville.org

Please feel free to contact us directly with any questions or concerns.



Thank you!



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

Sewer Line Install on Broadway (top left and right), Forming and pouring curb/gutter/sidewalk (bottom left and right)

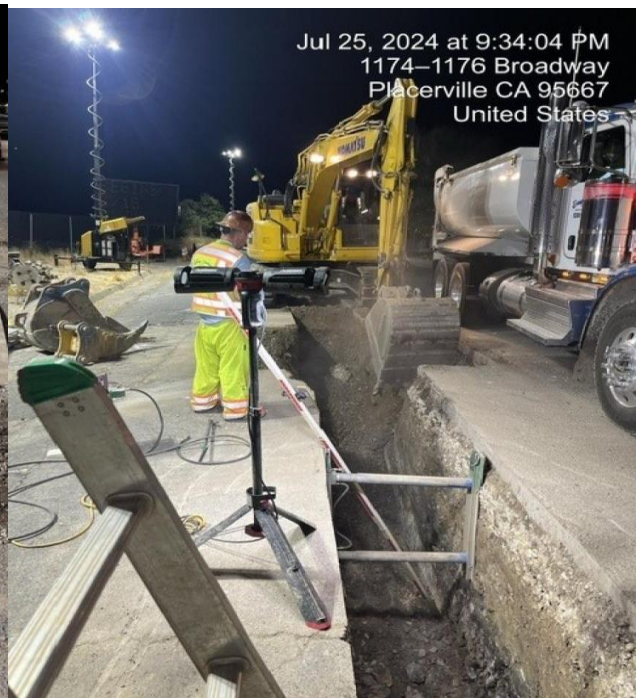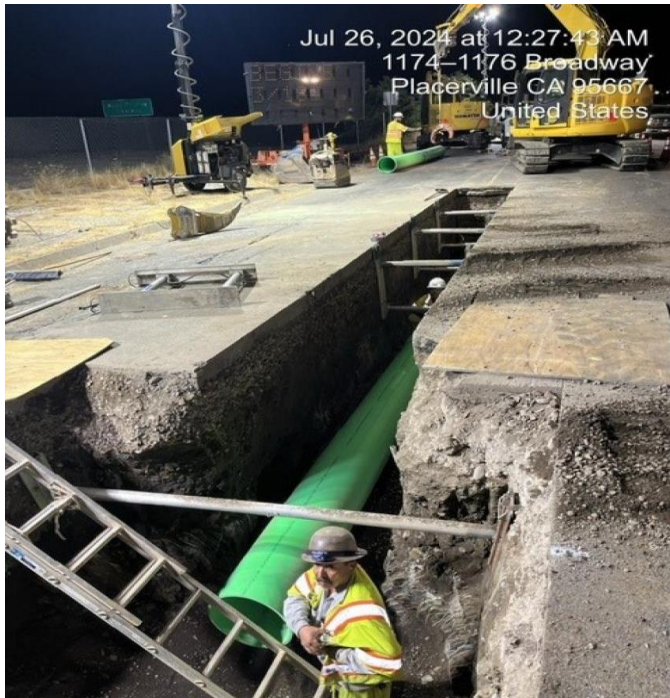

Thank you!
