



# BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

## CONSTRUCTION UPDATE #20

Week of August 12, 2024

Hi Everyone!

Construction has begun and these updates will be distributed regularly to keep the community up to date on the status of the projects. Thanks in advance for everyone's understanding and patience during construction.

### **Current Period**

- Contractor continues with forming and pouring the new curb, gutter, sidewalk, and driveways on the south side of Broadway at Blairs.
- Contractor started demolition and grading work at Broadway and Wiltse for the new curb, gutter, and sidewalk
- Night crew continues with the installation of the new 8-inch sewer line and manholes for the new sewer main that runs down the center of Broadway
- Traffic control measures will be in place to direct vehicles and pedestrians through the work areas, but there may be some minor delays.
- **Businesses near the project site and their access will remain open during all stages of construction.**

### **Following Period**

- **NIGHT WORK** - To help alleviate traffic congestion near the Broadway and Mosquito Road intersection, the Contractor will continue work operations to install the new 18-inch sewer and manholes down the center of Broadway. Approximately 4 more weeks of sewer line work which will be followed by broadband conduit installation.
- **DAY WORK** – Contractor will continue work operations on the south side of Broadway from Blairs to the east with the forming and pouring of the new curb, gutter, sidewalk, and driveways. Then work operations will move up to Broadway and Wiltse.

### **Important Information**

HWY 50 eastbound off-ramp at Broadway and Mosquito Road under HWY 50 will be closed at night due to nighttime work operations at the intersection of Mosquito Road and Broadway.

### **Contacts**

Dion Carr, Resident Engineer, Dewberry, (916) 276-4721, [dcarr@dewberry.com](mailto:dcarr@dewberry.com)

Melissa McConnell, City Engineer, City of Placerville, (530) 642-5250, [mmcconnell@cityofplacerville.org](mailto:mmcconnell@cityofplacerville.org)

*Please feel free to contact us directly with any questions or concerns.*


*Thank you!*



# BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

Sewer Line Install and Paving on Broadway (top left and right), Forming and pouring retaining wall (bottom left and right)

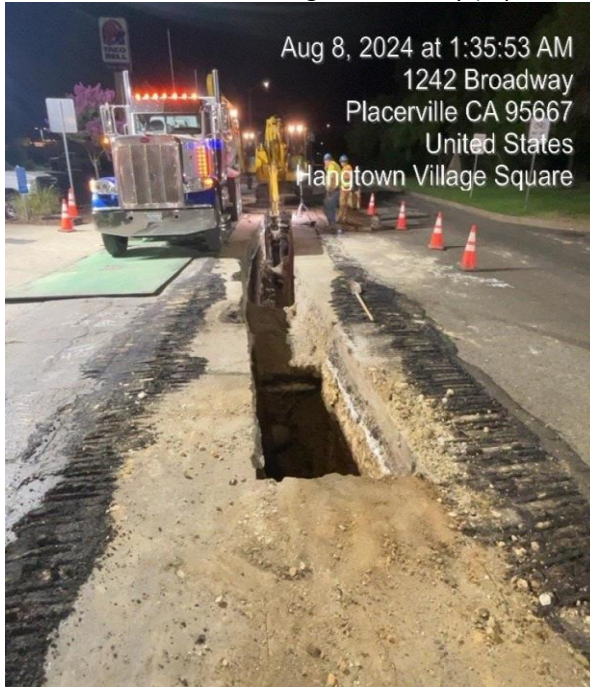

*Thank you!*
