



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

CONSTRUCTION UPDATE #24

Week of September 9, 2024

Hi Everyone!

Construction has begun and these updates will be distributed regularly to keep the community up to date on the status of the projects. Thanks in advance for everyone's understanding and patience during construction.

Current Period

- The Contractor will complete most of the daytime work operations by the end of this week by finishing up the asphalt paving conforms at the driveways, pouring the stairs at Wiltse, forming, and pouring the new curb ramps at Mosquito, and completing the miscellaneous minor concrete curb/gutter and sidewalk repairs on the western end of Broadway.
- The night crew is continuing with the installation of the new 8-inch sewer line and manholes on Broadway, but production has been slowed due to a significant amount of rock encountered during trenching.
- Traffic control measures will be in place to direct vehicles and pedestrians through the work areas, but there may be some minor delays.
- **Businesses near the project site and their access will remain open during all stages of construction.**

Following Period

- **NIGHT WORK** - To help alleviate traffic congestion near the Broadway and Mosquito Road intersection, the Contractor will continue work operations to install the new 18-inch sewer and manholes down the center of Broadway. Approximately 2 more weeks of sewer line work which will be followed by Broadband conduit installation and storm drain work.
- **DAY WORK** – Most daytime work operations will be concentrated at the western end of Broadway and should wrap up in the next couple of weeks.

Important Information

HWY 50 eastbound off-ramp at Broadway and Mosquito Road under HWY 50 will be closed at night due to nighttime work operations at the intersection of Mosquito Road and Broadway.

Contacts

Dion Carr, Resident Engineer, Dewberry, (916) 276-4721, dcarr@dewberry.com

Melissa McConnell, City Engineer, City of Placerville, (530) 642-5250, mmcconnell@cityofplacerville.org

Please feel free to contact us directly with any questions or concerns.


Thank you!



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

Pouring Sidewalk Ramp (top), Sewer Line Install on Broadway (bottom)

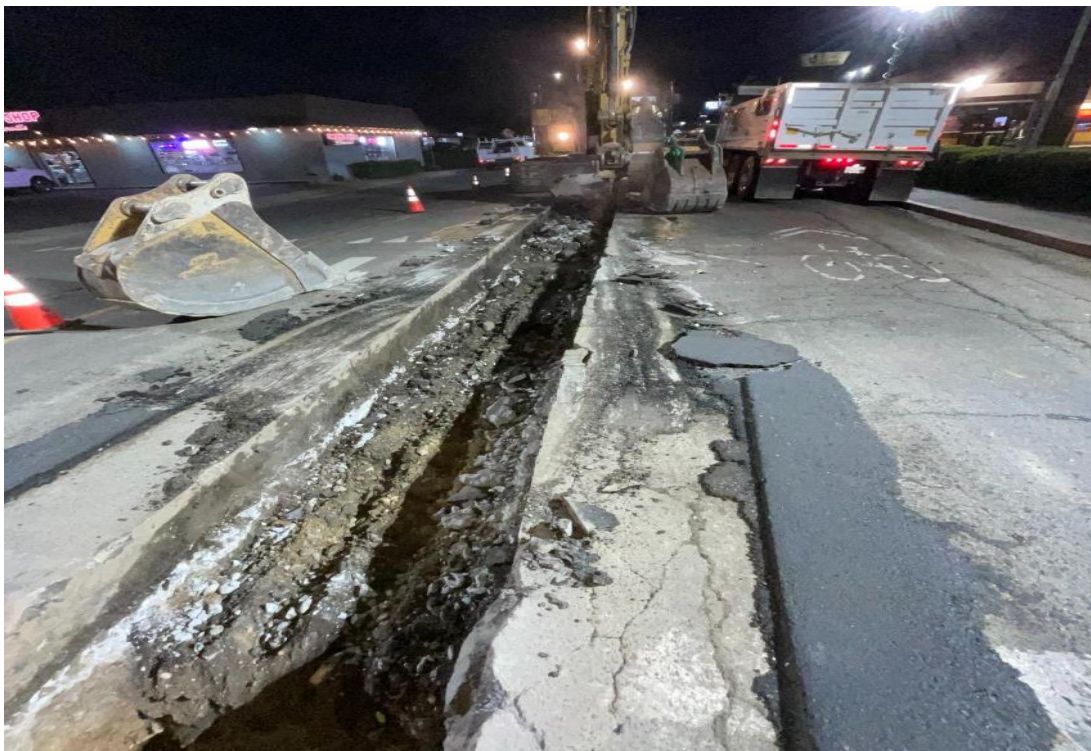

Thank you!
