



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

CONSTRUCTION UPDATE #27

Week of September 30, 2024

Hi Everyone!

Construction has begun and these updates will be distributed regularly to keep the community up to date on the status of the projects. Thanks in advance for everyone's understanding and patience during construction.

Current Period

- The Contractor has completed the minor concrete items during the day which included the stairs and sidewalk at Wiltse, along with the miscellaneous minor concrete curb/gutter and sidewalk repairs on the western end of Broadway.
- The Broadband conduit installation will be completed by the end of the week.
- The night crew is continuing with the storm drain work on Broadway and Schnell School Road.
- Traffic control measures will be in place to direct vehicles and pedestrians through the work areas, but there may be some minor delays.
- **Businesses near the project site and their access will remain open during all stages of construction.**

Following Period

- **NIGHT WORK** - The Contractor will finish the installation of the new storm drain lines at Schnell School Road and start the roadway reconstruction work operations.
- **DAY WORK** – Daytime work operations will be minimal over the next week, but there may be some minor work operations that take place. A section of the roadway reconstruction at Blairs and Broadway will occur during day in early October.

Important Information

HWY 50 eastbound off-ramp at Broadway will be closed intermittently at night due to nighttime work operations on Broadway.

Contacts

Dion Carr, Resident Engineer, Dewberry, (916) 276-4721, dcarr@dewberry.com

Melissa McConnell, City Engineer, City of Placerville, (530) 642-5250, mmcconnell@cityofplacerville.org

Please feel free to contact us directly with any questions or concerns.


Thank you!



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

Broadband Conduit Install (top), Sidewalk Pour (bottom)

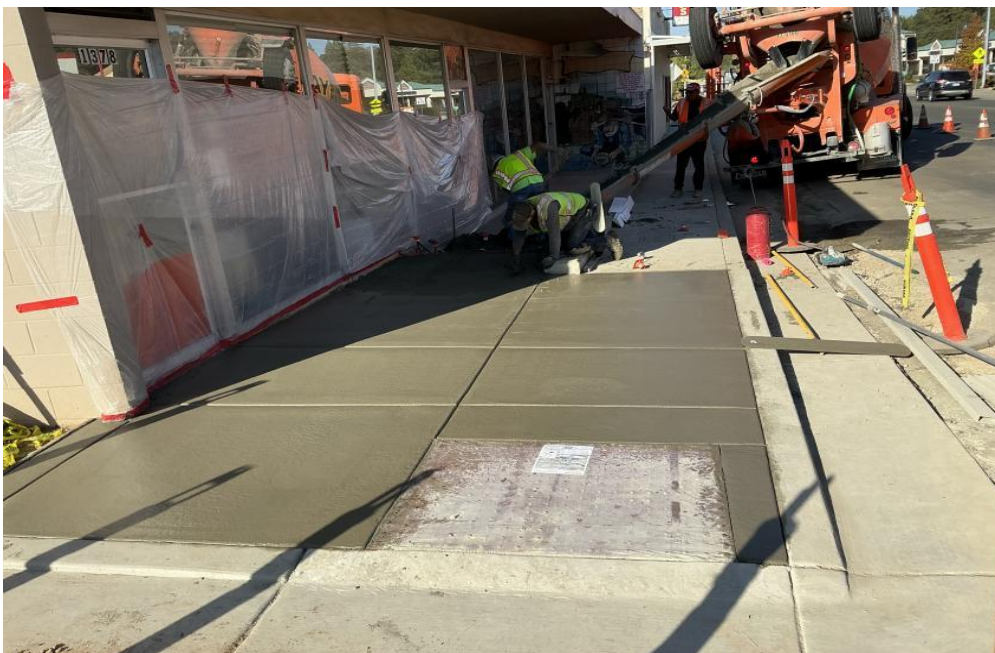

Thank you!
