



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

CONSTRUCTION UPDATE #22

Week of August 26, 2024

Hi Everyone!

Construction has begun and these updates will be distributed regularly to keep the community up to date on the status of the projects. Thanks in advance for everyone's understanding and patience during construction.

Current Period

- Contractor completed forming and pouring the new curb, gutter, sidewalk, and driveways on the south side of Broadway at Blairs will be completing the asphalt paving in the coming weeks.
- Contractor completed the grading work at Broadway and Wiltse and has already formed and poured some of the new curb, gutter, and sidewalk.
- Contractor also started some of the demolition and grading work at the 76 Gas Station
- The night crew is continuing with the installation of the new 8-inch sewer line and manholes on Broadway, production has been slowed due to a significant amount of rock encountered during trenching
- Traffic control measures will be in place to direct vehicles and pedestrians through the work areas, but there may be some minor delays.
- **Businesses near the project site and their access will remain open during all stages of construction.**

Following Period

- **NIGHT WORK** - To help alleviate traffic congestion near the Broadway and Mosquito Road intersection, the Contractor will continue work operations to install the new 18-inch sewer and manholes down the center of Broadway. Approximately 3 more weeks of sewer line work which will be followed by Broadband conduit installation.
- **DAY WORK** – Contractor will continue work operations at Wiltse with the forming and pouring of the new curb, gutter, and sidewalk. Then work operations will move down to the 76 Gas Station to form and pour the new improvements. Parking lot restoration work will also follow to finish the driveway areas.

Important Information

HWY 50 eastbound off-ramp at Broadway and Mosquito Road under HWY 50 will be closed at night due to nighttime work operations at the intersection of Mosquito Road and Broadway.

Contacts

Dion Carr, Resident Engineer, Dewberry, (916) 276-4721, dcarr@dewberry.com

Melissa McConnell, City Engineer, City of Placerville, (530) 642-5250, mmcconnell@cityofplacerville.org

Please feel free to contact us directly with any questions or concerns.


Thank you!



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

Pouring Seat Wall at Wiltse (top), Sewer Line Install on Broadway (bottom)

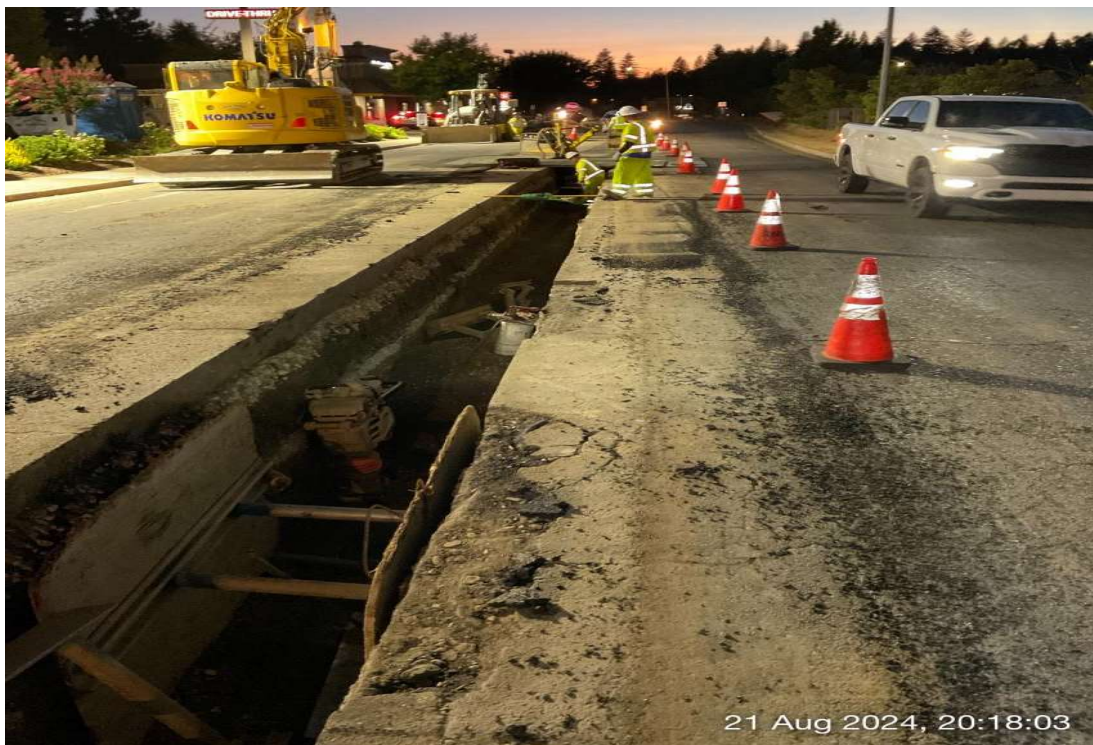

Thank you!
