

MOSQUITO ROAD STABILIZATION PROJECT – PHASE 1

CIP# 41819

CONSTRUCTION UPDATE #2

June 22, 2020

Hi Everyone!

This is an update to the community regarding the Mosquito Road Stabilization Project – Phase I. Construction began the second week in February, and these updates will continue to be sent via email to interested parties and posted on the City of Placerville's website to keep the community up-to-date on the status of this project. Each update will involve a summary of work completed the prior period, work being performed the current period, work anticipated the following period and any important information that may impact the community. Also, a project exhibit is attached. Thanks in advance for everyone's understanding and patience through this process.

Previous Period

- Installation of approximately 1,400 feet of new 8-inch C900 water main has been completed.
- Water main installation continues. Approximately 85% of water main replacement has been completed to date.
- 3 new fire hydrants have been installed.
- New water quality sampling station completed.
- Installation of approximately 1,400 feet of 8-inch sewer pipe lining has been completed. Sewer main lining is 100% complete.
- 4 new cast-in-place sewer manholes have been installed improving access for future sewer maintenance.

Current Period

- Installation of the last 260 feet of water main (Segment 2).
- Installation of 1 additional new fire hydrant.
- Installation of 13 new 1-inch residential water services and meters.
- Segment 2 water main be pressure tested, disinfected.
- 77 of 90 (86%) working days have been completed to date.
- Work on water pollution control measures and adherence to the project WPCP.
- Businesses near the project site and their access to Mosquito Road remain open and will continue to remain open during all stages of construction.

Following Period

- Segment 2 to be connected to City system and entered into service.
- Pipe trench paving and patch paving as interim roadway stabilization improvement prior to Mosquito Road Overlay.
- Water and sewer work to begin on Mosquito Road between US-50 and Clay Street.

- Notifications of service interruption will be mailed to affected customers, final connections will be scheduled, and the new system will be entered into service.

Important Information

Construction began the second week of February with sewer improvement work. All contract sewer work between Clay Street and the City Limit has been completed. Additional sewer improvement operations between US-50 and Clay Street are anticipated to begin in late July.

Installation of contract potable water improvements began on March, 30 2020 with approximately 1,400 feet of new 8-inch C900 water main completed to date. Water main replacement will continue until completed by the end of June. After the completion of water main replacement new residential water services and water meters will be installed.

Final connections to the City system will be installed adjacent to and within the intersection of Hocking Street and Mosquito Road, and Dimity Lane and Mosquito Road. Since these are intersections and Mosquito Road narrows at these locations, traffic control flaggers will be required, so motorists should anticipate slightly longer delays than they have experienced previously as the working zone moves on Mosquito Road. Access to business and homes will be preserved at all times.

Contacts

Cory Schiestel, City of Placerville (530) 642-5557 cschiestel@cityofplacerville.org
Resident Engineer


Bret Stone, City of Placerville (530) 642-5567 bstone@cityofplacerville.org
Construction Inspector

Rebecca Neves, City of Placerville (530) 642-5250 rneves@cityofplacerville.org
City Engineer

Please feel free to contact us directly with any questions or concerns



Pictured: Installation of a New Fire Hydrant at 2850 Mosquito Road

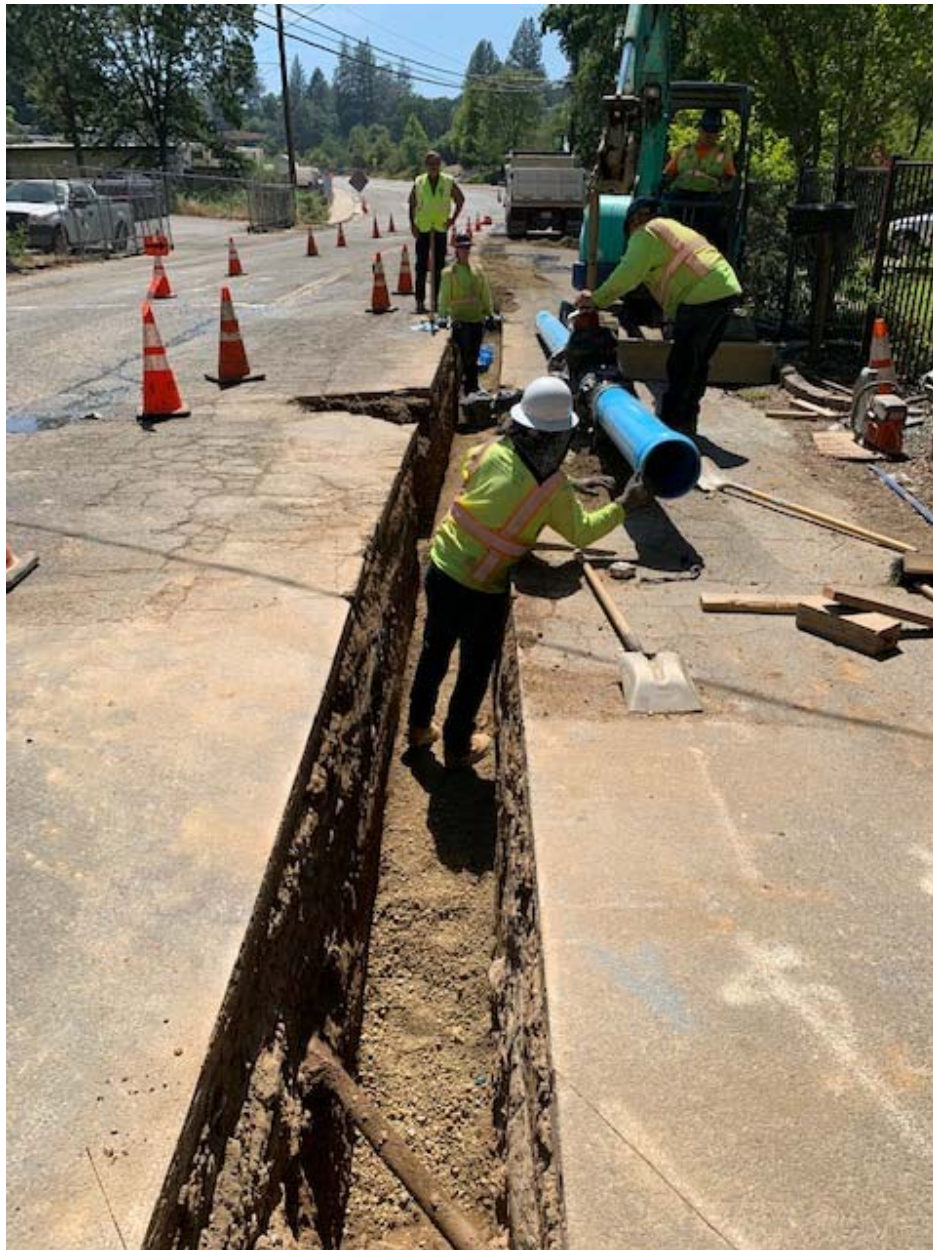

Pictured: Installation of New 8-inch Water Main within the Intersection of Dimity Lane and Mosquito Road (Note: The Existing 2-inch Steel Water Main can be seen in the Foreground)
