



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

CONSTRUCTION UPDATE #9

Week of June 3, 2024

Hi Everyone!

Construction has begun and these updates will be distributed regularly to keep the community up to date on the status of the projects. Thanks in advance for everyone's understanding and patience during construction.

Current Period

- Contractor has backfilled the retaining wall located across the street from Save Mart and has started to install the brick veneer – the pedestrian detour remains in place for this sidewalk closure.
- Contractor has completed the installation of the new Broadway water main and Stout Court water main and will be connecting them into the water system next week
- Contractor started installing the new 12-inch storm drain located east of the Broadway and Blairs intersection
- Contractor will continue with removal and reconstruction work operations on the north side of Broadway from Carson Road and working to the east.
- Traffic control measures will be in place to direct vehicles and pedestrians through the work areas, but there may be some minor delays.
- **Businesses near the project site and their access will remain open during all stages of construction.**

Following Period

- **NIGHT WORK** - To help alleviate traffic congestion near the Broadway and Mosquito Road intersection, the Contractor will start night work operations on June 10, 2024 to install a new 8-inch water main on Mosquito Road and a new 18-inch sewer on Broadway.
- **DAY WORK** – Contractor will continue with removal and sidewalk construction work on the north side of Broadway.

Important Information

There may be traffic delays at the HWY 50 eastbound off-ramp at Broadway due to the daytime work operations at the intersection of Mosquito Road and Broadway.

Contacts

Dion Carr, Resident Engineer, Dewberry, (916) 276-4721, dcarr@dewberry.com

Melissa McConnell, City Engineer, City of Placerville, (530) 642-5250, mmcconnell@cityofplacerville.org

Please feel free to contact us directly with any questions or concerns.

Thank you!



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

Brick veneer (top) and reconstruction work operations on north side of Broadway (bottom)




Thank you!



Google Maps

City of Placerville - Broadway Maintenance Project (CIP 42003)
Night work starting June 10, 2024

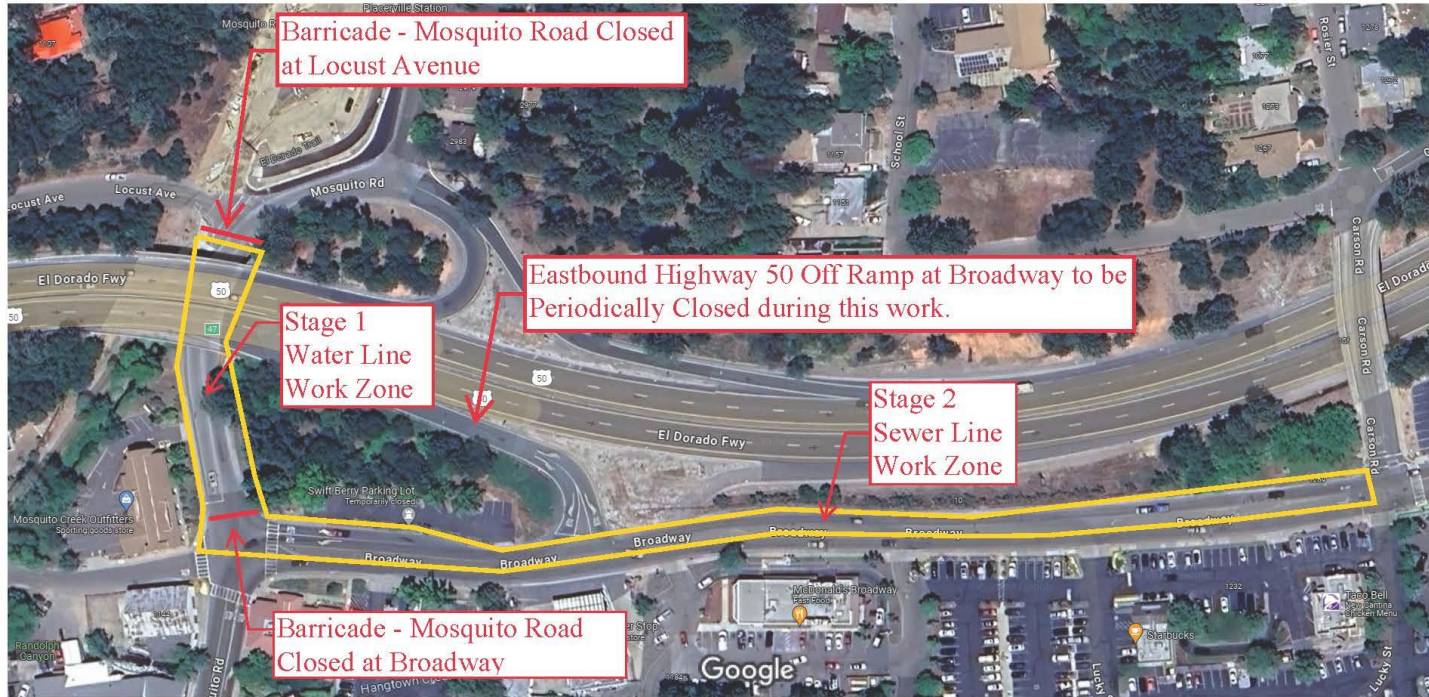

Imagery ©2024 Airbus, Maxar Technologies, Map data ©2024 Google 50 ft

Starting the week of June 10, 2024, the contractor will begin Stage 1 Water Line work on Mosquito Road necessitating a night closure of Mosquito Road between Locust Avenue and Broadway. Traffic control with flaggers and a detour route will be in place.

Then in Stage 2, sewer line work will begin on Broadway at the intersection with Mosquito Road and moving eastward under traffic control. Periodically, the Eastbound Highway 50 off-ramp will be closed during this night work with a detour in place.

Please pay close attention to traffic control, signage, and flaggers during this work.

Thank you!
