



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

CONSTRUCTION UPDATE #31

Week of October 28, 2024

Hi Everyone!

Construction has begun and these updates will be distributed regularly to keep the community up to date on the status of the projects. Thanks in advance for everyone's understanding and patience during construction.

Current Period

- The Contractor has completed the Broadway mainline asphalt paving work – Thank you to everyone for your patience during this major work operation.
- Daytime work for the upcoming week will include:
 - Asphalt removal and asphalt paving on Stout Court
 - Concrete finishing work
- Nighttime work for the upcoming week will include:
 - Adjusting utilities to grade on Broadway
 - Lay-out and preparation for upcoming striping and stamped crosswalk work
- Traffic control measures will be in place to direct vehicles and pedestrians through the work areas, but there may be some minor delays.
- **Businesses near the project site and their access will remain open during all stages of construction.**

Following Period

- **NIGHT WORK** – Finish up adjusting utilities to grade along with the stamped crosswalk work at Mosquito and Schnell School.
- **DAY WORK** – Daytime work operations will include: Broadway striping and sign installation along with finishing up miscellaneous concrete items.

Important Information

HWY 50 eastbound off-ramp at Broadway will be closed intermittently at night due to nighttime work operations on Broadway.

Contacts

Dion Carr, Resident Engineer, Dewberry, (916) 276-4721, dcarr@dewberry.com

Melissa McConnell, City Engineer, City of Placerville, (530) 642-5250, mmcconnell@cityofplacerville.org

Please feel free to contact us directly with any questions or concerns


Thank you!



BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

Final Mosquito and Broadway Paving (top and bottom)

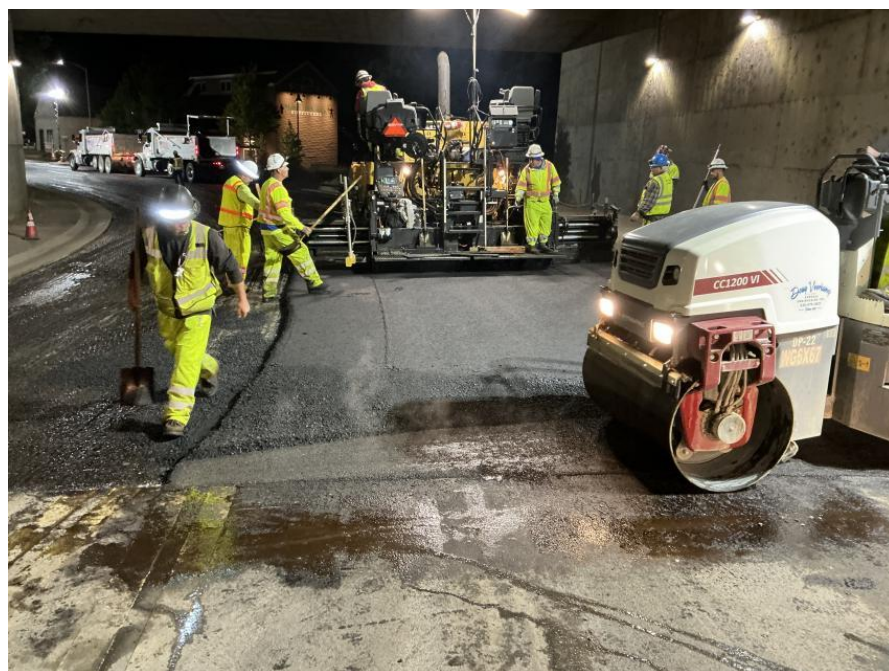

Thank you!
