



# BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

## CONSTRUCTION UPDATE #7

Week of May 13, 2024

Hi Everyone!

Construction has begun and these updates will be distributed regularly to keep the community up to date on the status of the projects. Thanks in advance for everyone's understanding and patience during construction.

### **Current Period**

- Construction continues at the retaining wall area located across the street from Save Mart. The wall has been poured and the contractor will be removing the forms and preparing the wall for the brick veneer – Pedestrian detour remains in place for this sidewalk closure
- Contractor continues excavate and install the new Broadway water main from the Splasherville Car Wash to the Blairs intersection – This water main will pass by several driveways on the south side of Broadway, but the driveways will remain open.
- Traffic control measures will be in place to direct vehicles and pedestrians through the work areas, but there may be some minor delays.
- Businesses near the project site and their access will remain open during all stages of construction.

### **Following Period**

- PG&E work operations at the intersection of Mosquito Road and Broadway have been suspended until July 2024.
- Contractor will start work operations to install a new water service for Stout Court
- To help alleviate traffic congestion near the Broadway and Mosquito Road intersection, the Contractor is planning night work operations in this area, in mid-June 2024 to install a new 8-inch water main on Mosquito Road and a new 18-inch sewer on Broadway.

### **Important Information**

There may be traffic delays at the HWY 50 eastbound off-ramp at Broadway due to the daytime work operations at the intersection of Mosquito Road and Broadway.

### **Contacts**

Dion Carr, Resident Engineer, Dewberry, (916) 276-4721, [dcarr@dewberry.com](mailto:dcarr@dewberry.com)

Melissa McConnell, Interim City Engineer, City of Placerville, (530) 642-5250, [mmcconnell@cityofplacerville.org](mailto:mmcconnell@cityofplacerville.org)

*Please feel free to contact us directly with any questions or concerns.*


*Thank you!*



# BROADWAY SIDEWALKS AND BROADWAY MAINTENANCE PROJECTS

CIP # 41606 and #42003

The new retaining wall progress across from Save Mart (top) and water line utility work at Wiltse (bottom).

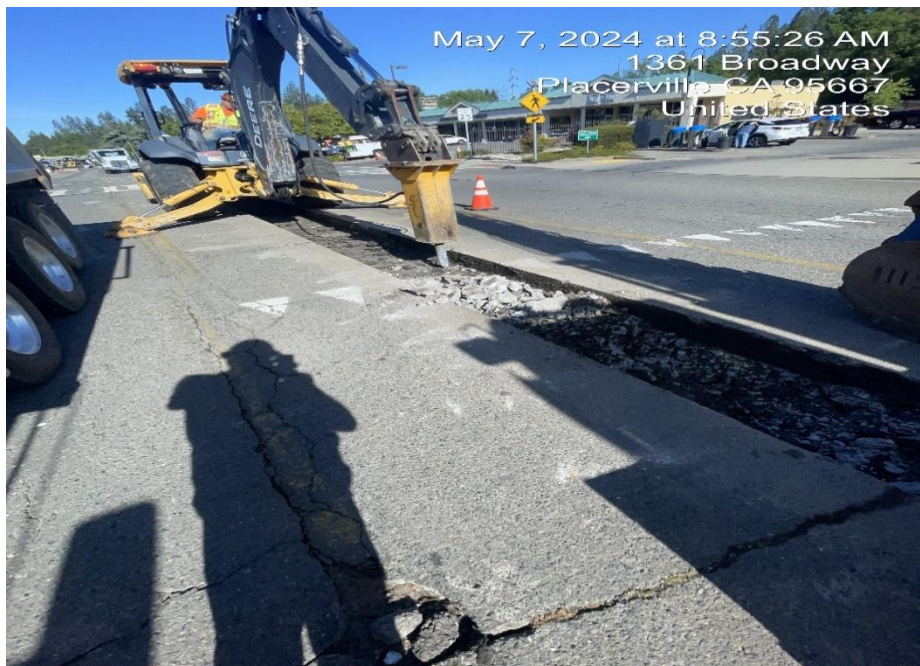

*Thank you!*
